


佐世地区 位置図

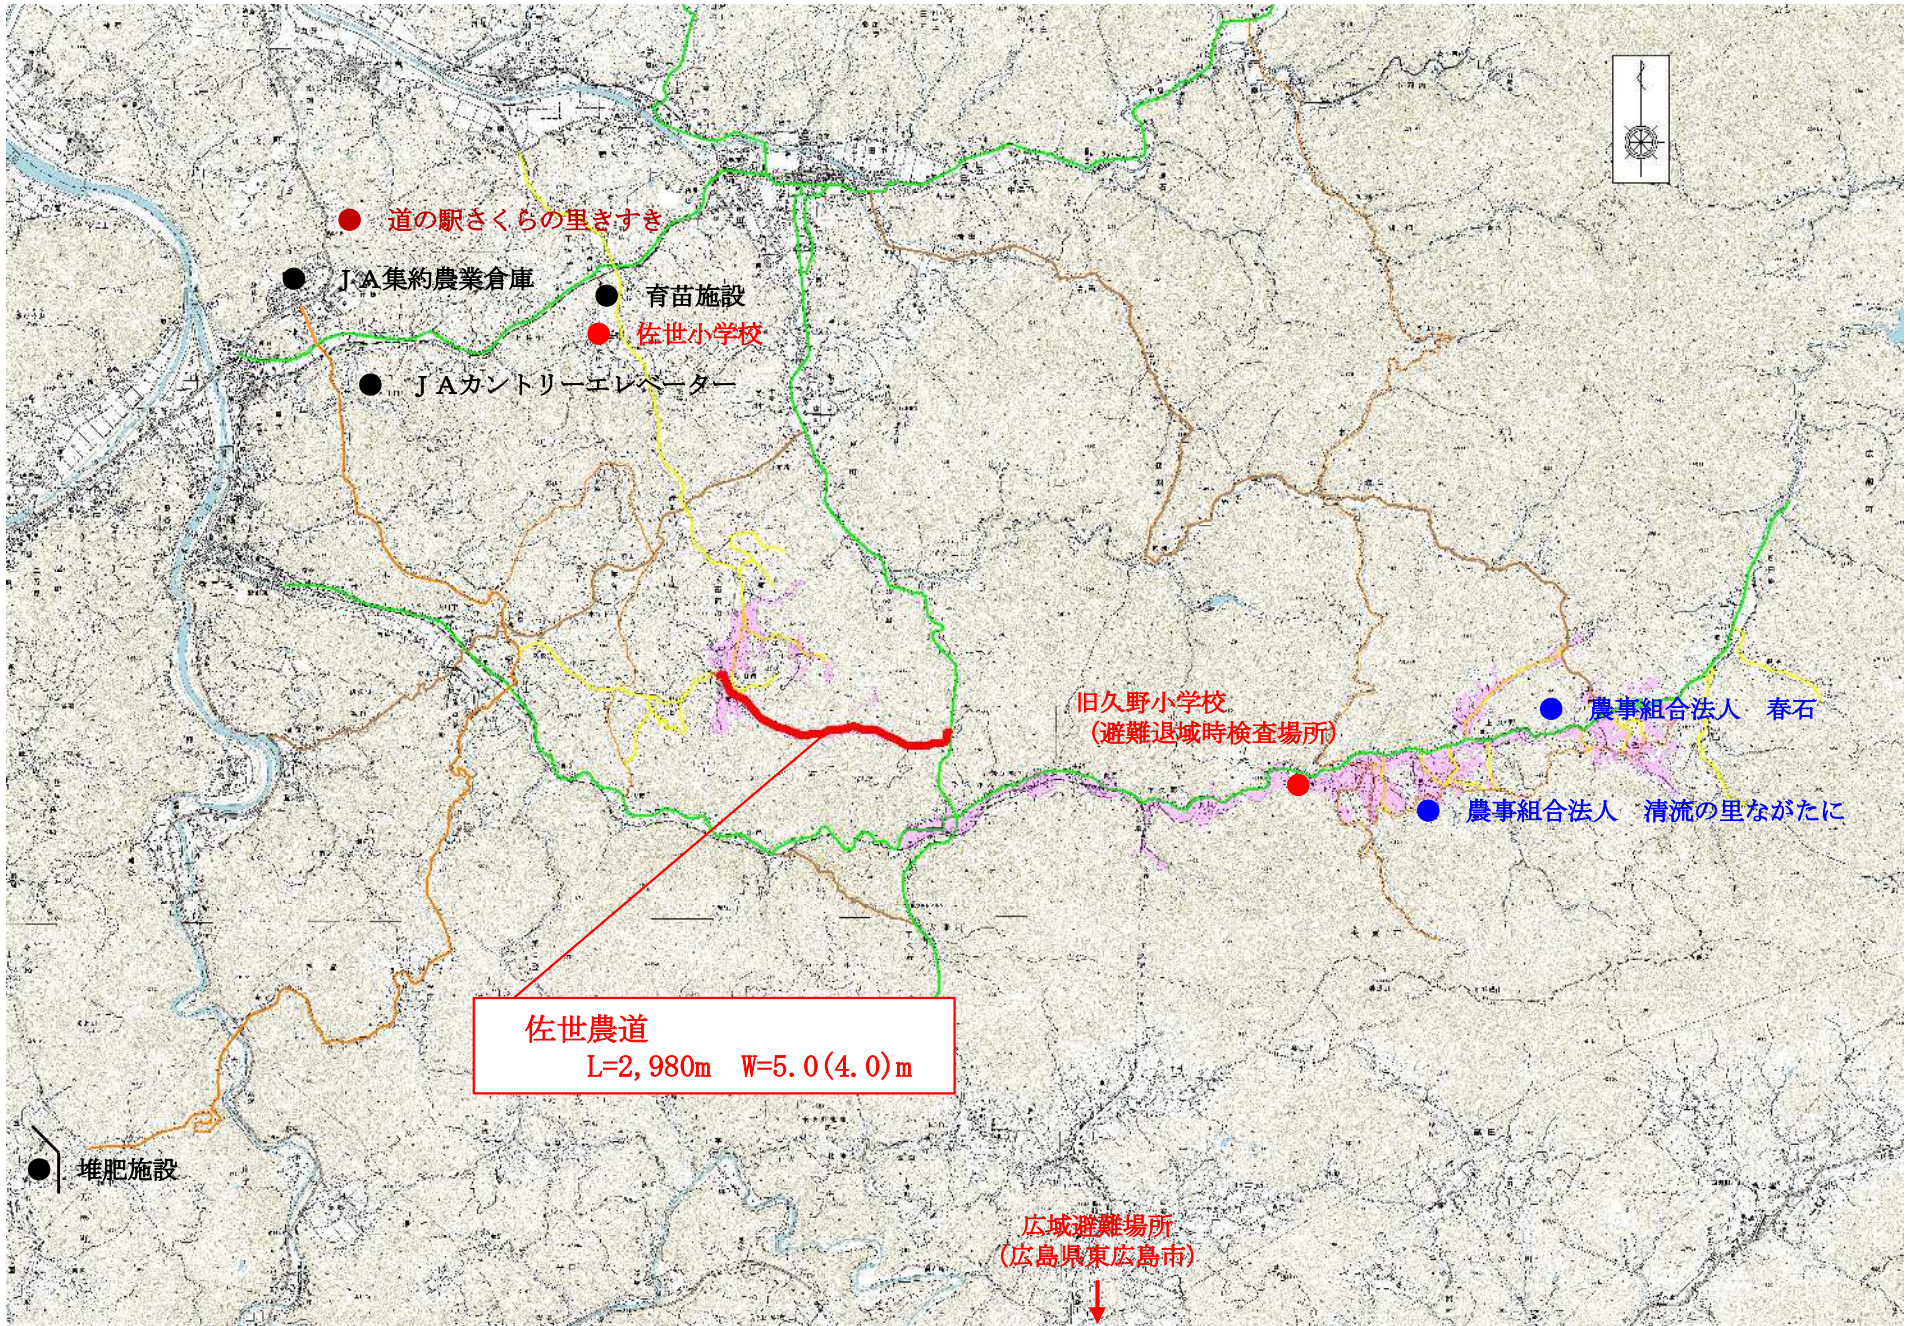

佐世地区 計画平面図

進捗状況 (事業費)		
総事業費	1,015,800千円	100%
R 7迄事業費	684,700千円	67.4%
R 8以降事業費	331,100千円	32.6%

進捗状況 (事業量)		
農道延長	2,980m	100%
道路・舗装工事完了区間	940m	31.5%
道路工事完了区間	1,130m	37.9%
道路工事未完了区間	1,850m	62.1%
舗装工事未完了区間	2,040m	68.5%

